

Date: Tuesday, 12/5/2006 8:11:44 AM
 User: Kim Johnston

Process Sheet

Customer : CU-DAR001 Dart Helicopters Services	Drawing Name : X-TUBE AS 350/355 HI AFT
Job Number : 29763A	
Estimate Number : 12483	
P.O. Number : <i>N/A</i>	Part Number : D350748241
This Issue : 12/5/2006 S.O. No. : <i>N/A</i>	Drawing Number : D350-748-241
Prsht Rev. : NC	Project Number : N/A
First Issue : <i>N/A</i> Type : LANDING GEAR	Drawing Revision : <i>C UNDER REVIEW D</i>
Previous Run : 29762A	Material : <i>N/A</i>
Written By : <i>[Signature]</i>	Due Date : 1/30/2007 Qty: 1 Um: Each
Checked & Approved By : <i>[Signature]</i>	
Comment : Est Rev: A New Issue 06-07-05 JLM Est Rev: B Update cadplate process 06-09-12 KJ	

Additional Product

Job Number:



Seq. #:	Machine Or Operation:	Description :
---------	-----------------------	---------------

1.0	DC	DOCUMENT CONTROL
-----	----	------------------

**Comment:** DOCUMENT CONTROL

Photocopy bluefile and create labels as per PPP D350-748-241 CHG001

N/A Packaged with 27829

2.0	D6018125	Crosstube Material
-----	----------	--------------------

**Comment:** Qty.: 1.0000 Each(s)/Unit Total : 1.0000 Each(s)

Crosstube Material

D6018-125

2.299" OD X 2.000" ID

Batch: *27472*

SG 06.12.07

3.0	MORI SEIKI	MORI SEIKI CNC LATHE LARGE
-----	------------	----------------------------

**Comment:** MORI SEIKI CNC LATHE LARGE

1-Fill tube with sand & install plugs on both ends as per Folio FA647

2-Turn first side as per Folio FA647

3-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D350-748-241.

SG 06.12.08

4.0	QC1	INSPECT ALL DIM TO DIM SHEET
-----	-----	------------------------------

**Comment:** INSPECT ALL DIM TO DIM SHEET

SG 06.12.08

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Tuesday, 12/5/2006 8:11:44 AM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI AFT

Job Number: 29763A

Part Number: D350748241

Job Number:



Seq. #:

Machine Or Operation:

Description :

5.0

MORI SEIKI

MORI SEIKI CNC LATHE LARGE



Comment: MORI SEIKI CNC LATHE LARGE

1-Turn second side as per Folio FA647

2-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D350-748-241.

3-Scribe part # as per Dwg D350-748-241

BC 06.12.08

1

6.0

QC1

INSPECT ALL DIM TO DIM SHEET



Comment: INSPECT ALL DIM TO DIM SHEET

BC 06.12.08

1

7.0

QC8

SECOND CHECK



Comment: SECOND CHECK

SA 06.12.08

1

8.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

Remove all Machining Marks

Pm/Job 06/12/13 ①

9.0

OUTSIDE SERVICE

OUTSIDE SERVICES



Comment: Sub-Contracting OUTSIDE SERVICES

Issue P/O: 2725

C206112115 ②

Heat Treat to min 180 KSI As per Dwg D350-748-241

Sand Blast tube after Heat Treat

Possible Supplier: Vac Aero

Ensure Certificate of Conformity is attached

10.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Receive & Inspect For Transit Damage

Ensure certificate of conformity is attached

R 7/1/17

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Tuesday, 12/5/2006 8:11:45 AM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI AFT

Job Number: 29763A

Part Number: D350748241

Job Number:



Seq. #:

Machine Or Operation:

Description :

11.0

QC6

DIMENSIONAL CHECK



Comment: DIMENSIONAL CHECK

12/07/04/29

12.0

HAND FINISHING1

HAND FINISHING RESOURCE #1



Comment: HAND FINISHING RESOURCE #1

Oil inside of tube with LPS-3.

A/R

LPS-3

Batch:

M103581

DP

7-3-15

13.0

BENDING

BENDING MACHINE



Comment: BENDING MACHINE

Bend tube as per Dwg D350-748-241 using CNC bender program D350A and Folio FT

DP 7-3-15

14.0

QC6

DIMENSIONAL CHECK



Comment: DIMENSIONAL CHECK

12/07/03/21

15.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Remove all marks from tube within limits of D350-748-241

2-Drill Tube as per Dwg D350-748-241 Using DT8876 Drill Jigs,
Set-up drill table as per QSI 010

3-Deburr

4-Engrave Part # and Batch # as per Dwg D350-748-241

Job 7-4-17

25
07-05-08

16.0

QC6

DIMENSIONAL CHECK



Comment: DIMENSIONAL CHECK

12/06.13. ①

17.0

OUTSIDE SERVICE

OUTSIDE SERVICES



Comment: Sub-Contracting OUTSIDE SERVICES

Issue P/O:

3975

CLO 7/06/14 ①

Stress relief at 375° for 5 hours

Magnetic Particle Inspect per ASTM E1444

Cadium Plate per QQ-P-416F, Class 1, Type 2

Dart Aerospace Ltd

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Tuesday, 12/5/2006 8:11:45 AM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI AFT

Job Number: 29763A

Part Number: D350748241

Job Number:



Seq. #:

Machine Or Operation:

Description :

Embrittle relief at 375° for 8 hours, Chromate Treat
Possible Supplier: Southwest United Industries
Ensure Certificate of Conformity is attached

18.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Receive & Inspect For Transit Damage
Ensure certificate of conformity is attached

CP 07/07/09

19.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

2407-10 ①

20.0

SPRAY PAINTING

SPRAY PAINTING



Comment: SPRAY PAINTING

1-Prime inside crosstube as per QSI 005 4.2

2-Paint Outside of Tube as per Dart QSI 005 4.2

> ml 070710 ①

21.0

QC14

Inspect Spray Paint



Comment: Inspect Spray Paint

Then, Wrap in plastic bag to protect from scratches

RT 07-07-12

22.0

D35021

SUPPORT



Comment: Qty.: 2.0000 Each(s)/Unit Total : 2.0000 Each(s)

SUPPORT

Batch: *28476*

RT 07-07-12

23.0

D2856400

Abrasion Strip



Comment: Qty.: 1.2401 f(s)/Unit Total : 1.2401 f(s)

Abrasion Strip 7.10" long x2

Batch: *32020*

RT 07-07-12

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Tuesday, 12/5/2006 8:11:45 AM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI AFT

Job Number: 29763A

Part Number: D350748241

Job Number:



Seq. #:

Machine Or Operation:

Description :

24.0

ALS41032225

Insert



Comment: Qty.: 1.0000 Each(s)/Unit Total : 1.0000 Each(s)

Insert

Batch:

~~10251~~ 19393

RT 07-07-12

25.0

AN960JD10

Washer



Comment: Qty.: 1.0000 Each(s)/Unit Total : 1.0000 Each(s)

Washer

Batch:

100151

RT 07-07-12

26.0

MS2192020

Clamp (per MIL-DTL-8783C)



Comment: Qty.: 2.0000 Each(s)/Unit Total : 2.0000 Each(s)

Clamp (per MIL-DTL-8783C)

Batch:

102712

RT 07-07-12

27.0

MS27039110

Screw



Comment: Qty.: 1.0000 Each(s)/Unit Total : 1.0000 Each(s)

Screw

Batch:

18836

RT 07-07-12

28.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Install Ground wire Insert, then insert screw and washer

2-Install Abrasion strips as per Dwg D350-748-241 & QSI 035.

3-Install supports Using Dt8876 as per Dwg D350-748-241, Torque to 60-80 IN-LBS

} RT 07-07-12

29.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

on 07/07/12 (x1)

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: 12 Date: 01/07/16
 QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Tuesday, 12/5/2006 8:11:45 AM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI AFT

Job Number: 29763A

Part Number: D350748241

Job Number:



Seq. #:

Machine Or Operation:

Description :

30.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Identify and pack for shipping as per PPP D350-748-241

Location: _____

PPP Rev: _____

1 PPPB 27829

1 12/7/12

31.0

QC21

FINAL INSPECTION/W/O RELEASE



Comment: FINAL INSPECTION/W/O RELEASE

12/10/12

Job Completion



CU 12-07-12

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector


Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Crosstube Bend Dimension Sheet

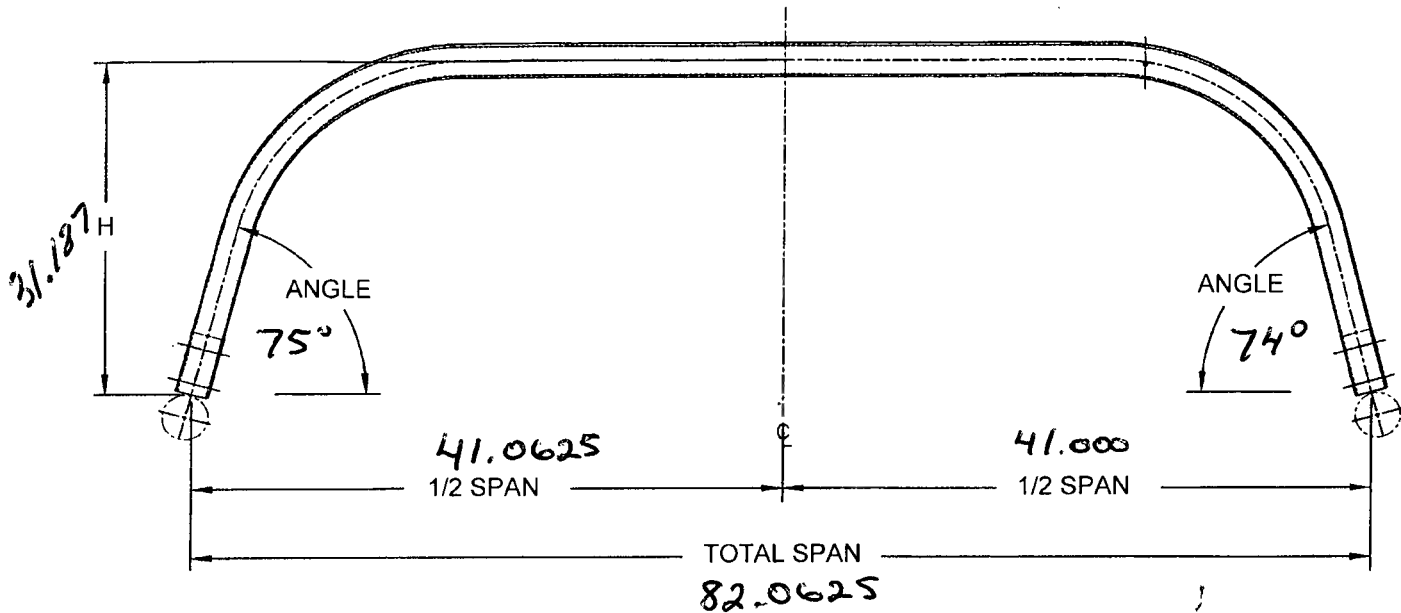

PART NUMBER: 350 748 241

BATCH NUMBER: 29763A

DRAWING: 0350748241 REVISION: D

H: 31.35

1/2 SPAN: 40.9

TOTAL SPAN: 81.8

ANGLE: 75°

QC 15: M

DATE: 07/03/21

QTY: ①

DART

DESIGN <i>GP</i>	DRAWN BY <i>GP</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>HH</i>	APPROVED <i>HH</i>	DRAWING NO. D350-748-241	REV. D SHEET 1 OF 3
DATE 06.10.31		TITLE CROSSTUBE (AS 350/355 HI AFT) NTS	
A	06.03.31	NEW ISSUE	
B	06.06.30	ADD D6018-125 & PRIME AND PAINT	
C	06.08.14	ADD CAD PLATING	
D	06.10.31	MAG. PARTICLE AND CAD PLATE AS MFD.	

RELEASED06.10.31 *HH*

QTY	P/N	DESCRIPTION
X	D350-748-241	CROSSTUBE ASSEMBLY (AS 350/355 HI AFT)
1	D6018-125	CROSSTUBE (OR D6015-125)
2	D3502-1	SUPPORT
2	D2856-400-710	ABRASION STRIP
1	AELS-1032-225	INSERT
1	AN960JD10	WASHER
2	MS21920-20	CLAMP (PER DART SPEC. M-MS21920-20)
1	MS27039-1-10	SCREW


D350-748-141 CROSSTUBE:

- 1) MATERIAL: MANUFACTURED FROM D6018-125 OR D6015-125
FINISHED LENGTH = 122.70±0.06
- 2) MACHINE PER MACHINING DETAIL ON PAGE 3. BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITIONS SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- 3) SCRIBE DART PART NUMBER AND BATCH NUMBER IN THIS AREA WITH VIBRATING STYLUS.
- 4) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 5) HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS 2759-1C AFTER TURNING
- 6) FINISH: MAGNETIC PARTICLE INSPECT PER DART QSI 038 4.2
CADMIUM PLATE PER AMS-QQ-P-416B, CLASS 1, TYPE II
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 7) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.
- 8) INSTALL D2856-400-710 ABRASION STRIP WITH A GAP ON BOTTOM SIDE OF CROSSTUBE, CENTERED OPPOSITE D3502-1 SUPPORT, PER QSI 035.
- 9) TORQUE MS21920-20 CLAMPS 60 TO 80 IN-LB
- 10) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- 11) ALL DIMENSIONS ARE IN INCHES
- 12) PART IS SYMMETRIC ABOUT CENTERLINE EXCEPT FOR Ø0.297 HOLE.

TO COPY
RETURN TO
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 29163A


Copyright © 2006 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

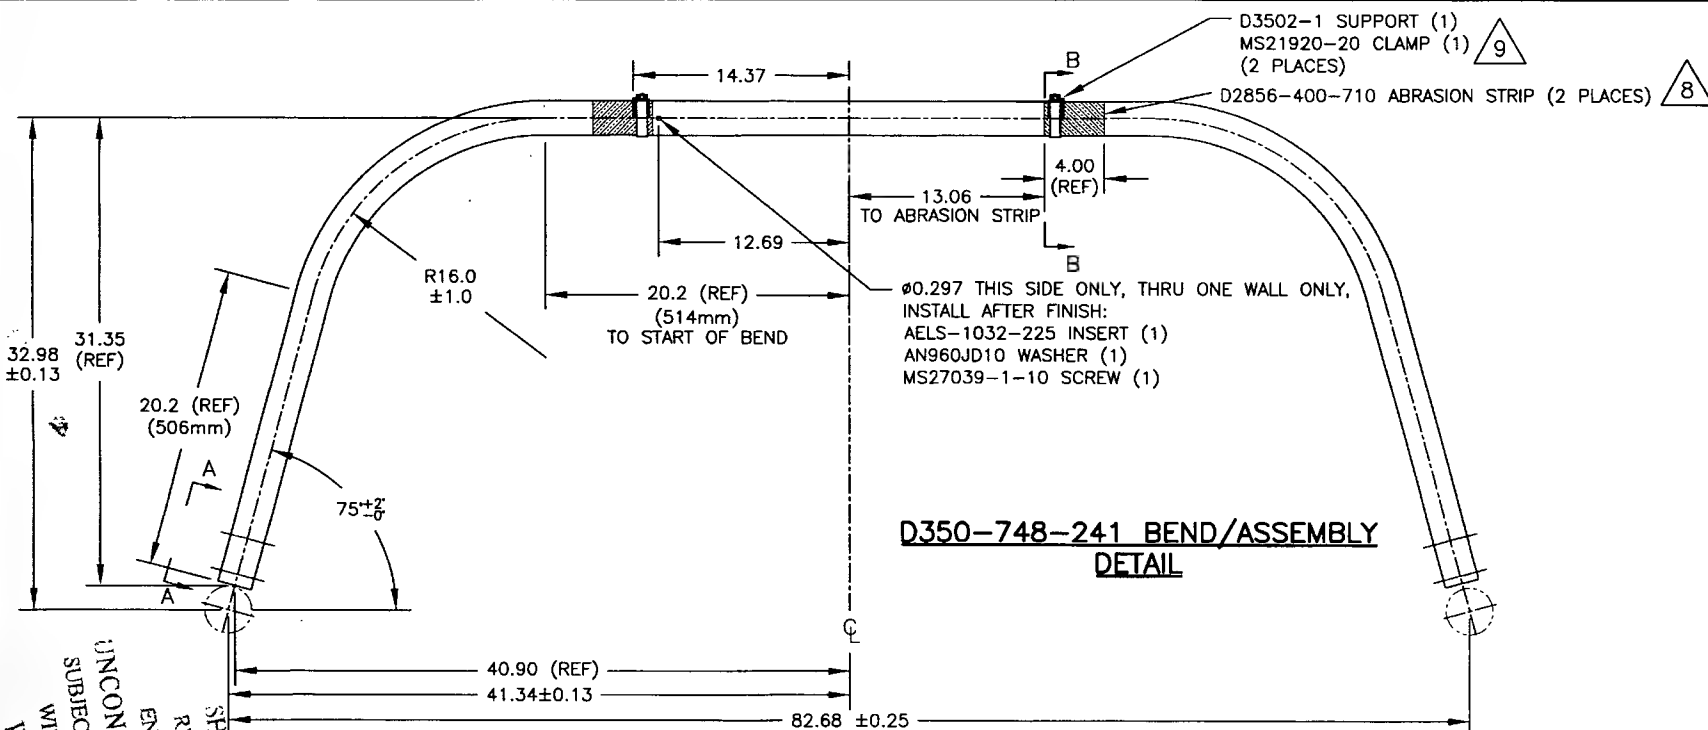


**D350-748-241 BEND/ASSEMBLY
DETAIL**

**SECTION B-B
SCALE 1:2**



**VIEW A-A
SCALE 1:2**

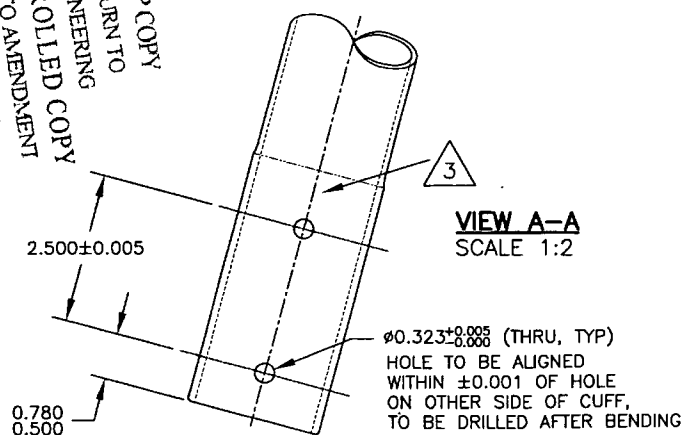

RELEASED


06-10-31

COPYRIGHT © 2006 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.



DESIGN qp	DRAWN BY qp	DART	DART AEROSPACE LTD. HARRISBURG, ONTARIO, CANADA
CHECKED #	APPROVED #	DRAWING NO. D350-748-241	REV. D SHEET 2 OF 3
DATE 06.10.31	TITLE CROSSTUBE (AS 350/355 HI AFT)	SCALE 1:8	

NO. 29763A
WORK ORDER
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
SHOP COPY
RETURN TO
ENGINEERING

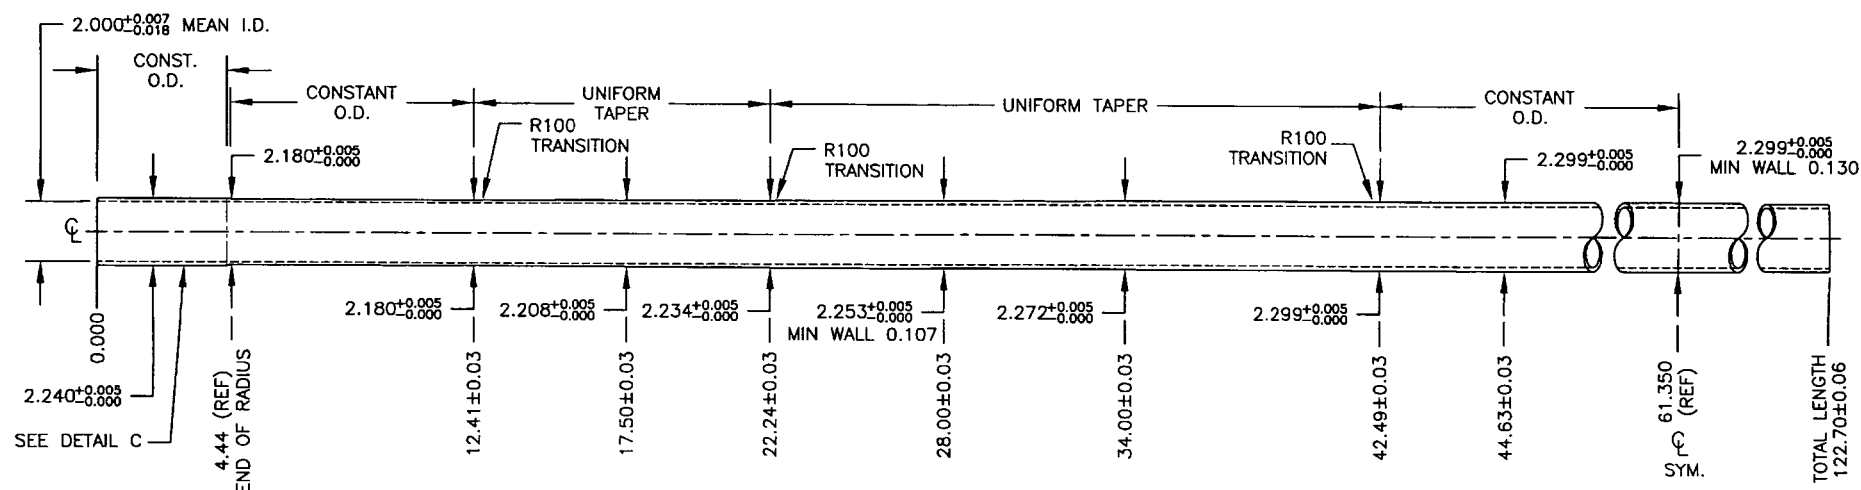

D350-748-241 MACHINING DETAIL

**DETAIL C: CUFF
SCALE 1:1**

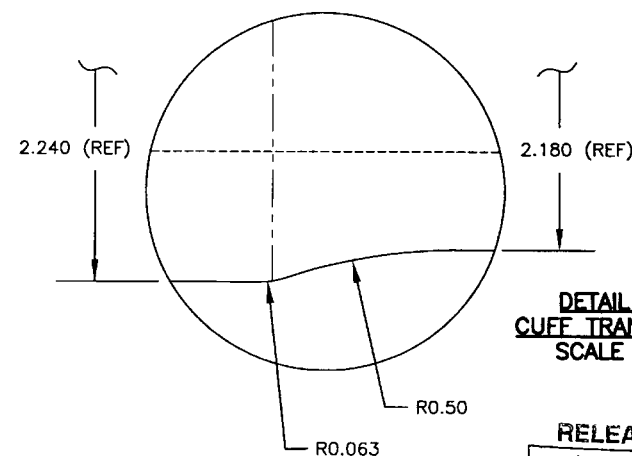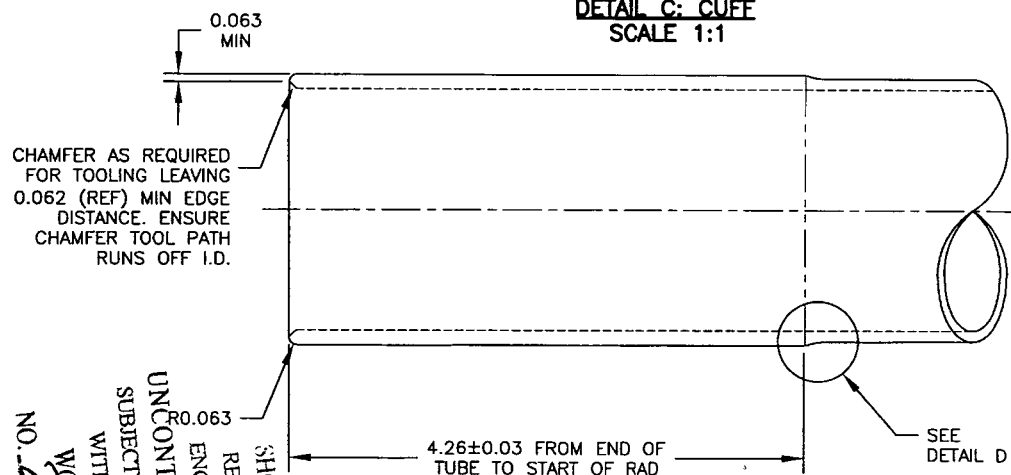

**DETAIL D:
CUFF TRANSITION
SCALE 9:1**

RELEASED

06.10.31

NO. 29763A
WORK COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
RETURN TO
ENGINEERING
UNCONTROLLED COPY

COPYRIGHT © 2008 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

DESIGN qp	DRAWN BY qp	DART	DART AEROSPACE LTD. WILLOWDALE, ONTARIO, CANADA
CHECKED #	APPROVED #	DRAWING NO. D350-748-241	REV. D
DATE 06.10.31	TITLE CROSSTUBE (AS 350/355 HI AFT)	SHEET 3 OF 3	SCALE 1:4

DART AEROSPACE LTD		Work Order:
Description: Crosstube Assembly		Part Number: D350748241
Inspection Dwg: D350-748-24 Rev: C		Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST

☒ First Article ☐ Prototype

Inspection Sheet Drawing Dimension		Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
SIDE A	2.240	+0.005 -0.000	2.242	-			
	2.180	+0.005 -0.000	2.185	-			
	2.208	+0.005 -0.000	2.212	-			
	2.234	+0.005 -0.000	2.238	-			
	2.253	+0.005 -0.000	2.256	-			
	2.272	+0.005 -0.000	2.277	-			
	2.299	+0.005 -0.000	2.301	-			
	.063	+0.010 -0.000	.063	-			
	R.50	+0.010 -0.000	.500	-			
	4.26	+0.030 -0.000	4.26	-			
SIDE B	2.240	+0.005 -0.000	2.242	-			
	2.180	+0.005 -0.000	2.185	-			
	2.208	+0.005 -0.000	2.212	-			
	2.234	+0.005 -0.000	2.237	-			
	2.253	+0.005 -0.000	2.256	-			
	2.272	+0.005 -0.000	2.276	-			
	2.299	+0.005 -0.000	2.301	-			
	.063	+0.010 -0.000	.063	-			
	R.50	+0.010 -0.000	.500	-			
	4.26	+0.030 -0.000	4.26	-			
	122.7	±0.06	122.7	-			

Measured by: BG	Audited by: SA	Prototype Approval:	N/A
Date: 06.12.08	Date: 06.12.08	Date:	N/A

Rev	Date	Change	Revised by	Approved
A		New Issue	KJ/JLM	

DART AEROSPACE LTD		Work Order:	
Description: Crosstube Assembly (AS350/355 High Aft)		Part Number:	D350-748-241
Inspection Dwg: D350-748-241 Rev: C		Page 1 of 1	

FIRST ARTICLE INSPECTION CHECKLIST

☒ **First Article**
☐ **Prototype**

Inspection Sheet Drawing Dimension		Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
SIDE A							
SIDE B							

Measured by:		Audited by:		Prototype Approval:	
Date:		Date:		Date:	

Rev	Date	Change	Revised by	Approved
A		New Issue (P/O D350-748-201)	KJ/JLM	



VAC AERO
INTERNATIONAL INC.

RELEASE NO

GST No. : R105468102

OAK 82647-1



HEAD OFFICE
1371 SPEERS ROAD, OAKVILLE, ONTARIO
CANADA L6L 2X5
TEL: (905) 827-4171 FAX: (905) 827-7489



2009 WYECROFT ROAD, UNIT B
OAKVILLE, ONTARIO
CANADA L6I 6J4
TEL: (905) 827-7377 FAX: (905) 827-1380



QUEBEC DIVISION
7450 RUE VÉRITÉ STREET, ST. LAURENT, QUÉBEC
CANADA H4S 1C5
TEL: (514) 334-4240 FAX: (514) 334-6269

01/11/2007

MM/DD/YYYY

PAGE : 1

1DAR01
BILL TO: DART AEROSPACE LTD.
1270 ABERDEEN ST.
HAWKESBURY, ON

SHIP TO : DART AEROSPACE LTD.
1270 ABERDEEN ST.
HAWKESBURY, ON

K6A 1K7

K6A 1K7

DATE SHIPPED	SHIP VIA	F.O.B.
01/11/2007	EPIC EXPRESS	ORIGIN
CUSTOMER P/O No.	JOB No.	TERMS
PO00002725		COD

PART No.	DESCRIPTION	UOM	QTY ORD	QTY SHPD	TEST RESULTS
D350-CROSS TUBES D350-748-141/-241		EA	8	8	
<p>Process Specifications: Procedure: 4353 HEAT TREATED TO 180-200 KSI PER AMS 2759-1C 100% HARDNESS TESTED PER ASTM E-18 HRC 40-43 MATERIAL: 4130</p> <p>REF. PS# 59054 RE: B29758A, B29757A, B29760A, B29765A, B29761A, B29764A, B29763A, B29762A</p> <p><i>[Signature]</i></p> <p>100% HARDNESS TESTED 8 pcs. 42/43 HRC</p> <p><i>[Signature]</i></p> <p>VA.I.O. TH. 25 Q.C.</p>					

I hereby certify that the material covered by this release note has been inspected and tested and conforms to all specifications relevant thereto in accordance with the conditions of the contract / or purchase order.

ON BEHALF OF VAC AERO INTERNATIONAL INC



[Signature]
Authorized Q.C. Inspector



VACUUM BRAZING · HEAT TREATING · SPECIAL PROCESSING · FURNACE EQUIPMENT
TURBINE COMPONENT OVERHAUL · PLASMA AND OTHER COATINGS



**CERTIFICATE OF
CONFORMANCE**

**CADORATH PLATING CO. LTD.
2150 LOGAN AVENUE
WINNIPEG, MANITOBA R2J-0J1**

DATE: Jun-29-2007

CONSIGNEE TO: Dart Aerospace Ltd.
1270 Aberdeen St.
Hawksbury, ON K6A 1K7

W/O #: 68047

INVOICE #: 35047

**CONTRACT OR
PURCHASE ORDER #**

P000003975

DESCRIPTION: SKID

QTY

1

P/N # D350748241

S/N # B29763

**MPI IAW ASTM-E-1444. CADMIUM PLATE IAW AMS-QQ-P-416 TYPE 2
CLASS 2. BAKE HEAT CART #7951 AND 7997**

CERTIFICATE: I certify that the items indicated here on have
been inspected and tested and conform to all specifications
and requirements detailed on the contract or purchase order.

Approved Inspector:

William Marozzola



Packing Slip



Cadorath Plating Co. Ltd.

2150 Logan Avenue, Winnipeg, Manitoba R2R-0J2

Phone: (204) 633-9420 Fax: (204) 633-8033

INVOICE NUMBER:

35047

Sold To

Dart Aerospace Ltd.
1270 Aberdeen St.

Hawksbury, ON K6A 1K7

Ship To:

Net 2% Interest Per Month charged on Overdue Accounts.

Any claims for shortages, overcharges, or damaged goods must be made within seven (7) days from receipt of goods.

Customer Order #:	Date Received:	Terms:	G.S.T. #:	Ship Via:	Ship Date:
P000003975	Jun-19-2007	NET 30 DAYS	10071 6547 RT0001		Jun-29-2007

Item # Qty P/N & Description

1	1 EA	SKID	S/N B31017
		P/N D350748141	W/O 68044
2	1 EA	SKID	S/N B31015
		P/N D350748141	W/O 68045
3	1 EA	SKID	S/N B29761
		P/N D350748241	W/O 68046
4	1 EA	SKID	S/N B29763
		P/N D350748241	W/O 68047
5	1 EA	SKID	S/N B28777
		P/N D350748241	W/O 68048
